




THE SCHOOL DISTRICT OF
PHILADELPHIA

School Year 2020-2021 Reopening

Hybrid Learning Implementation Pathway

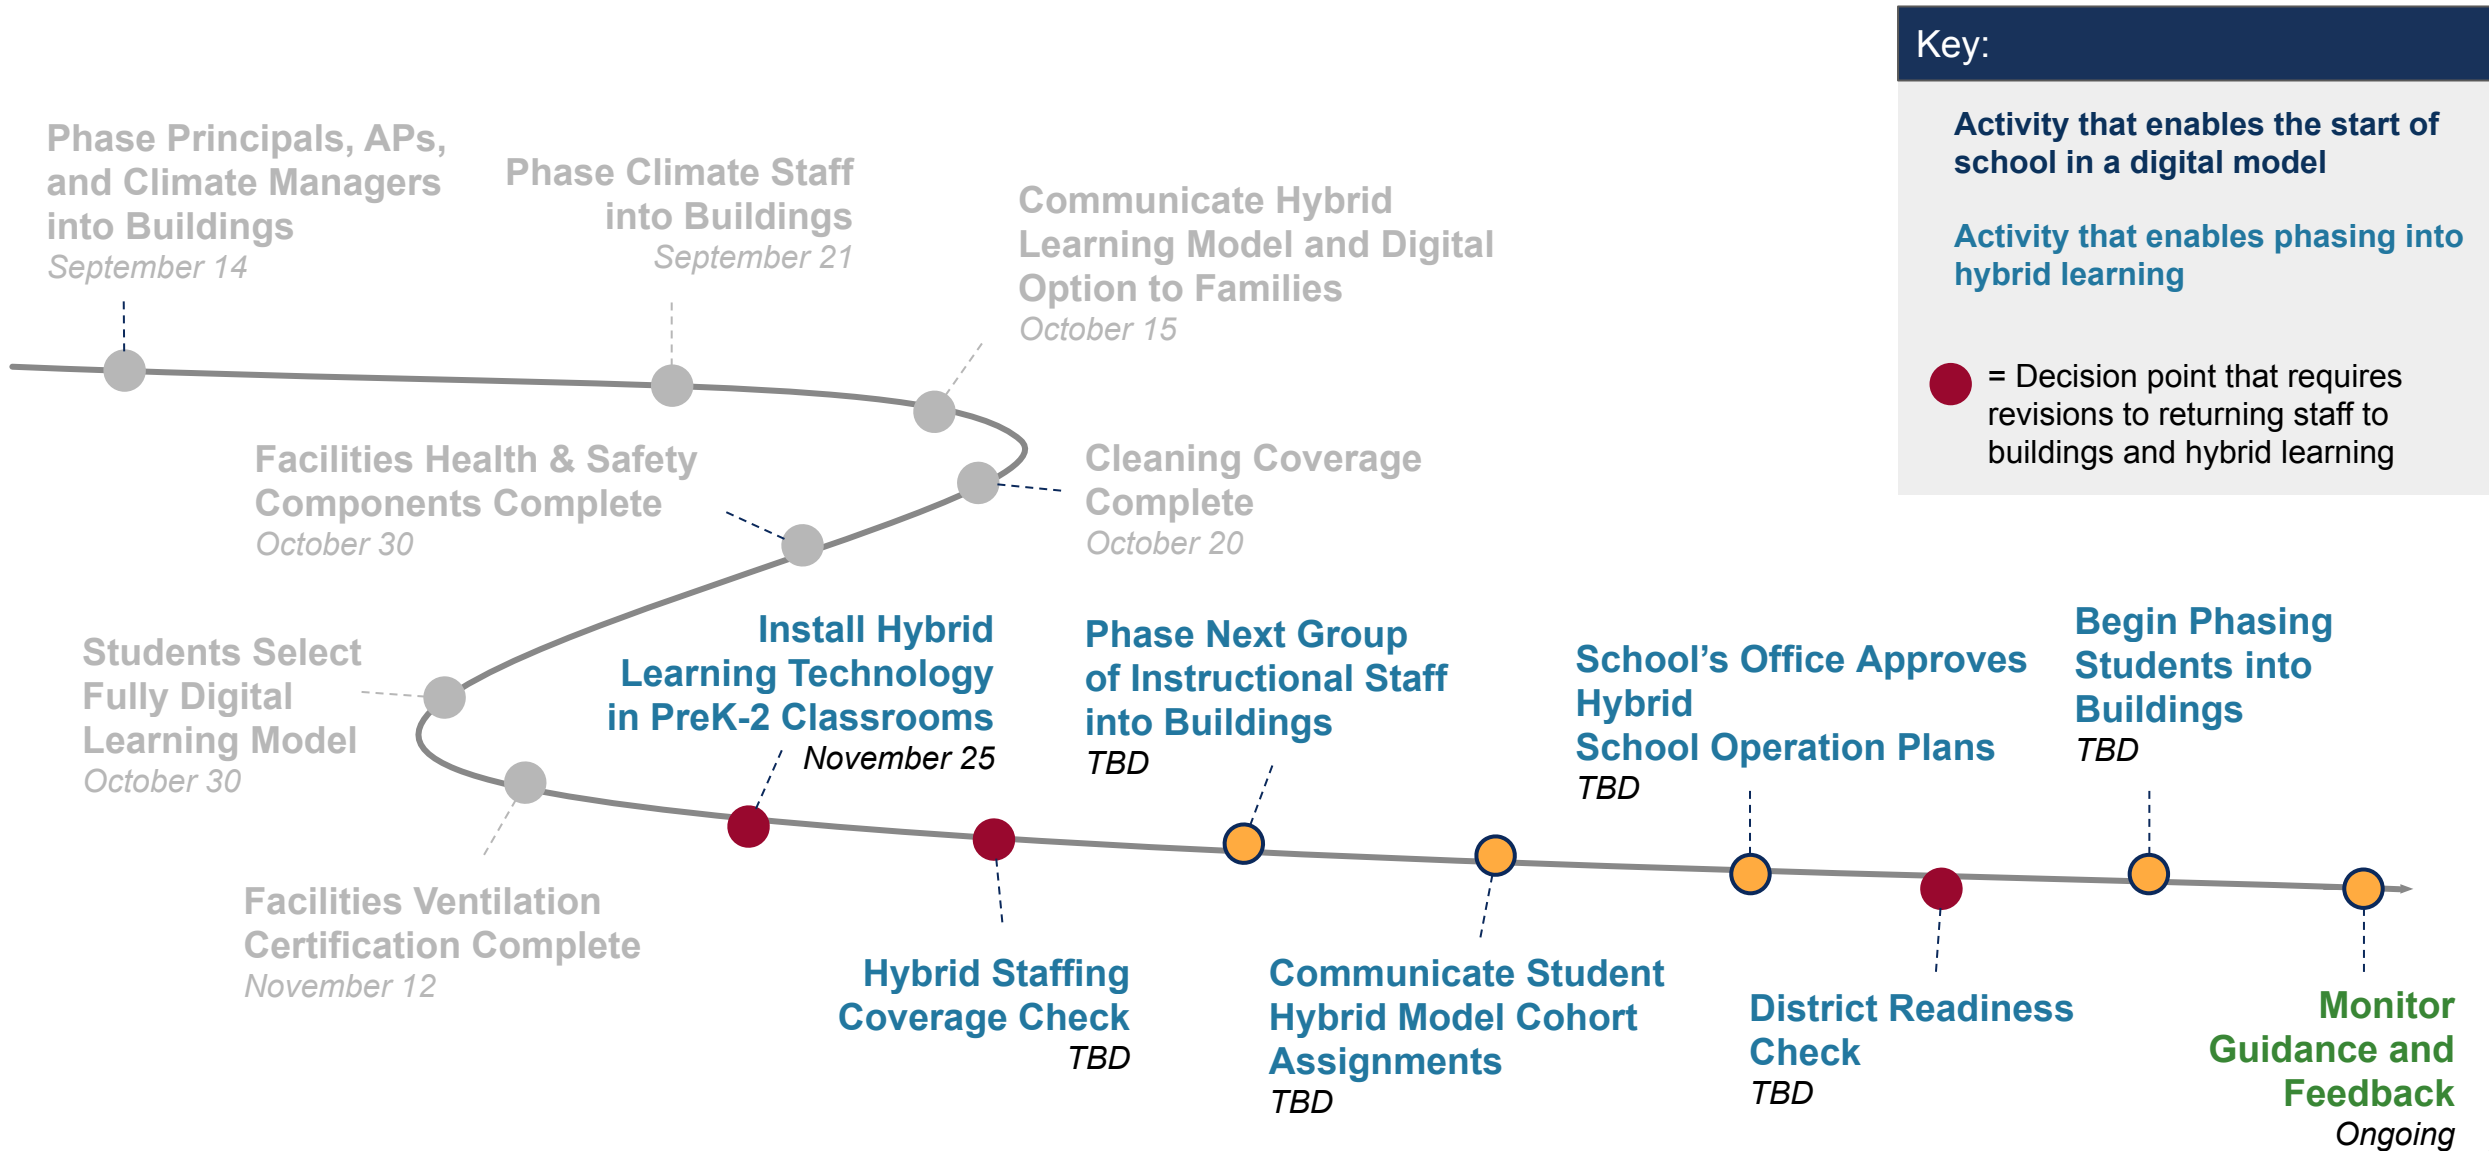

NOTE: It is possible that activities are not completed in this specific order, as many will be happening in parallel. This is exemplary.

Return to Learn - Reopening Readiness Report

Overall Status:



Digital Enablement



Enable students to be successful by providing devices, access to internet, an effective Learning Management System, and technology supports.

Academics



Establish enrollment and deliver an instructional model that is seamless across the learning model continuum, is aligned to grade-level instructional goals, and includes social emotional learning curriculum.

Staff Coverage



Have proper staff coverage and clearly outlined and communicated roles and responsibilities.

Building Readiness



Enable District buildings for a safe opening with the necessary supplies and updates, such as ventilation.

People Preparedness



Train, inform, and otherwise prepare the District (students, staff, and families) for reopening.

School Operational Readiness



Implement updated school operation plans with health and safety procedures installed and transportation and meal distribution solidified.

Digital Enablement




Enable students to be successful by providing devices, access to internet, an effective Learning Management System, and technology supports.

Leading Indicators

Devices

Number of Students Provided a Device vs. Have Not Received a Device

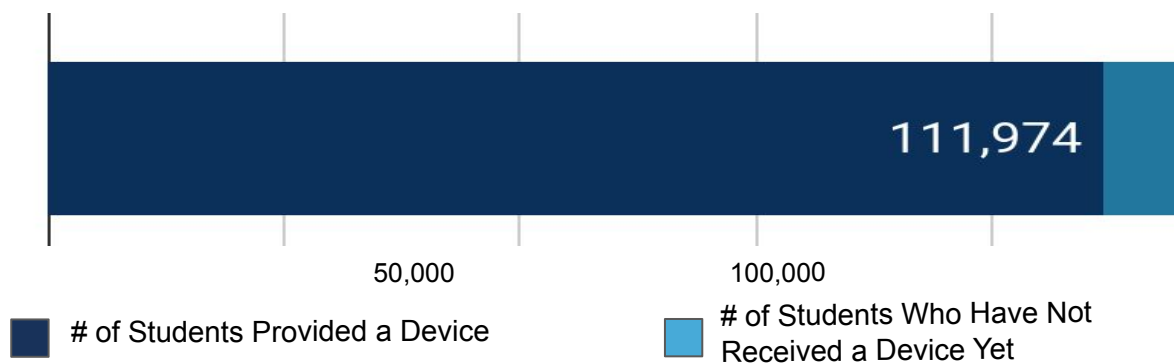

Internet Access

PHLConnectED

1,201

Total Number of Students Connected to Internet through PHL ConnectED

564

Number of Student Codes Activated

637

Number of Hot Spots Provided

Upcoming Key Activities

Activities	Deadline
Continue distributing Chromebooks at schools	End of November

Critical Issues and Risks

Reaching families in need of internet access

- Mitigation Plan:
 - Continued outreach to targeted families including home visits


Digital Enablement




Enable students to be successful by providing devices, access to internet, an effective Learning Management System, and technology supports.

Leading Indicators

Technology In-Hand

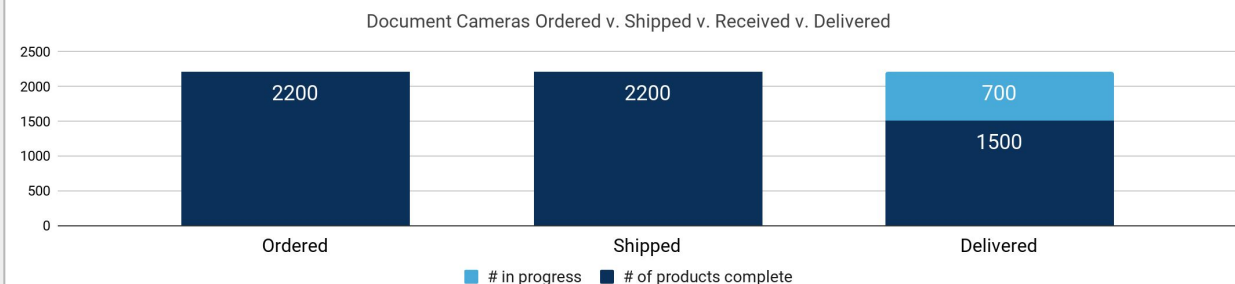

Installation and Training

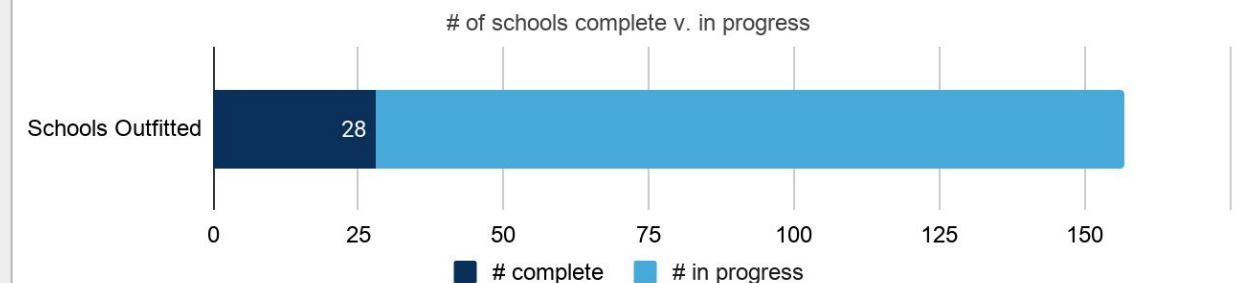


Upcoming Key Activities

Activities	Deadline
Work with schools to identify classrooms for installation	Ongoing

Critical Issues and Risks

None at this time

Academics



Establish enrollment and deliver an instructional model that is seamless across the learning model continuum, is aligned to grade-level instructional goals, and includes social emotional learning curriculum.

Leading Indicators

100%

Guidance for Hybrid Instruction Drafted

100%

Updated Guidance for Hybrid Support for Students with IEPs and English Learners Drafted

100%

Guidance for Hybrid Instruction Finalized

100%

Updated Guidance for Hybrid Support for Students with IEPs and English Learners Finalized

Upcoming Key Activities

Activities	Deadline
Review Q1 data to determine areas of strength and areas to develop	Ongoing

Critical Issues and Risks

None at this time


Staff Coverage



Have proper staff coverage and clearly outlined and communicated roles and responsibilities.

Leading Indicators

% Roles Filled

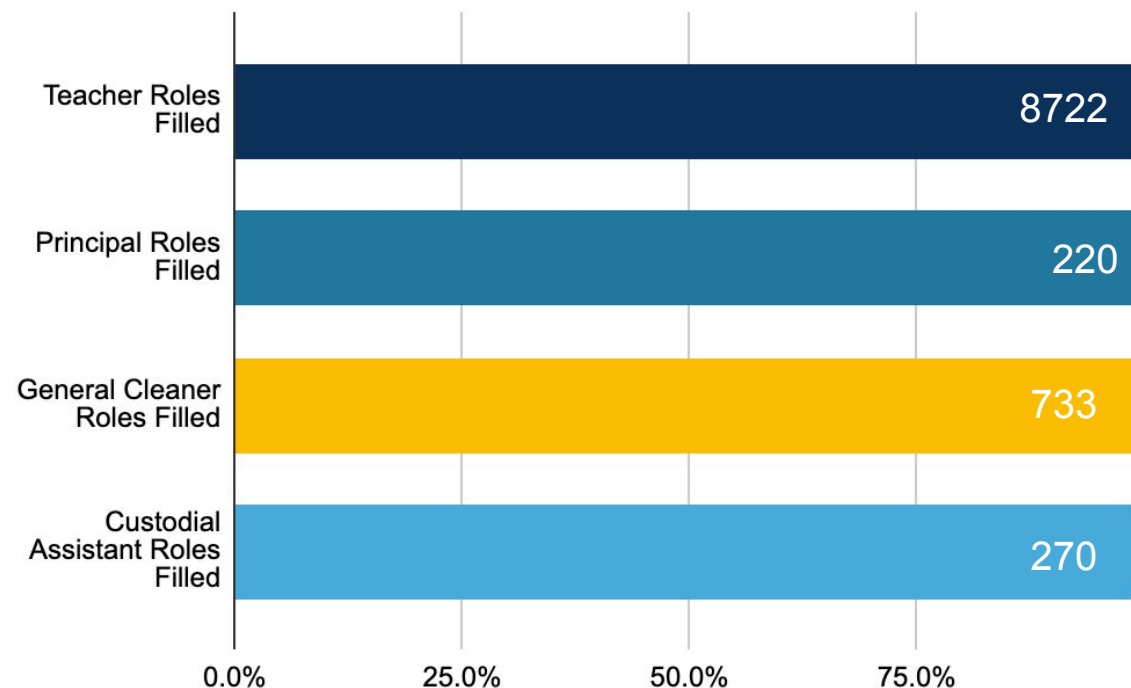

Upcoming Key Activities


Activities	Deadline
Hybrid staffing coverage check	TBD

Critical Issues and Risks

Ensuring we have an adequate number of substitutes for a return to buildings


- Mitigation plan:
 - Continuing to hire building subs
 - Utilizing new hiring incentives

Building Readiness




Enable District buildings for a safe opening with the necessary supplies and updates, such as ventilation.


Leading Indicators



Health and Safety Measures

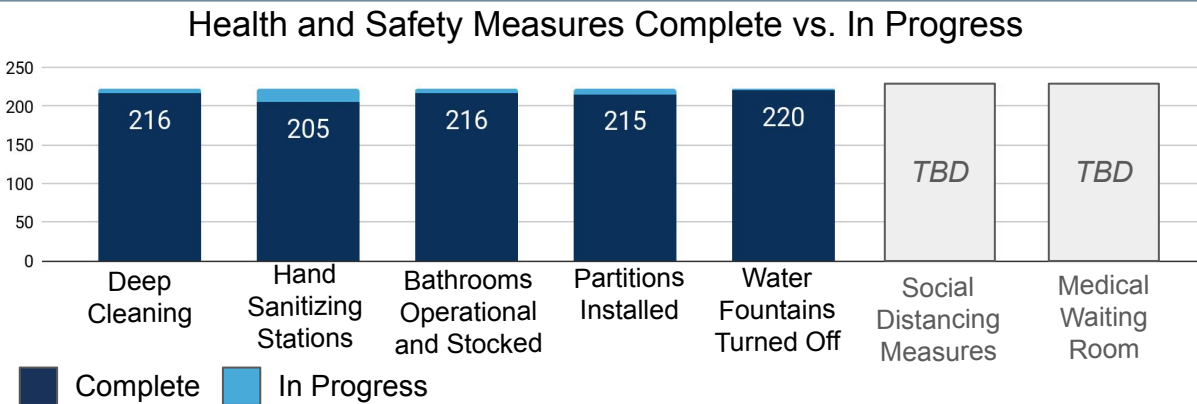

Ventilation



Upcoming Key Activities


Activities	Deadline
Onboard newly-hired General Cleaners	Ongoing
Building walkthroughs with SDP leadership and union partners	Ongoing

Critical Issues and Risks

Ventilation Challenges:

- Mitigation Plan:
 - Establish alternate fresh air flow


People Preparedness




Train, inform, and otherwise prepare the District (students, staff, and families) for reopening.

Leading Indicators

Number of Professional Development Sessions Planned vs. Delivered for Q1

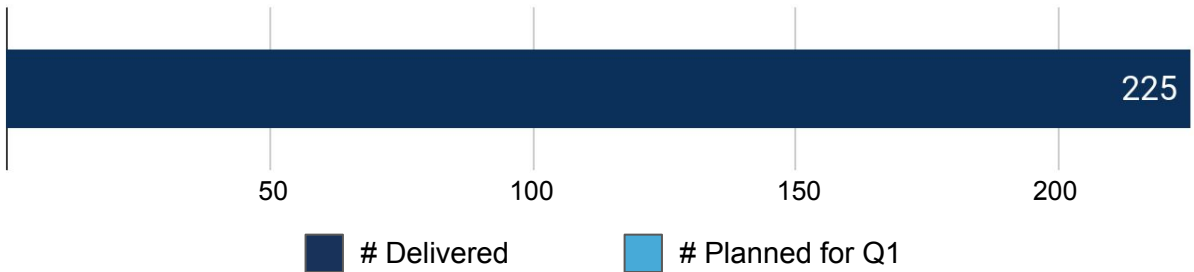

Number of Planned vs. Delivered PD for Hybrid PreK-2 Phase-in

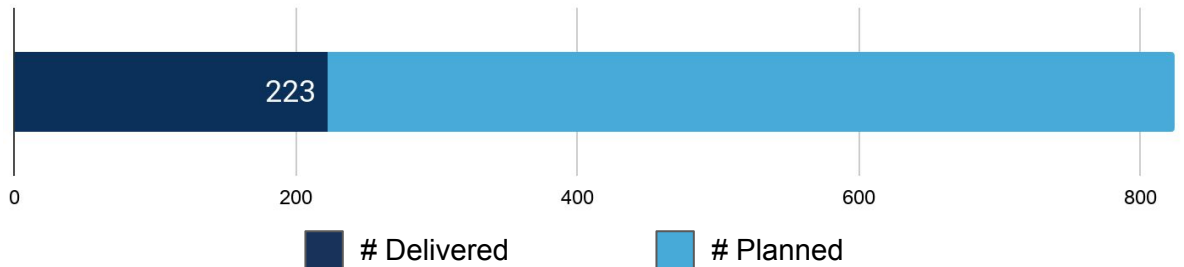

50%

% of School Reopening Communications Plan Executed

Upcoming Key Activities

Activities	Deadline
Deliver professional development for teachers phasing into hybrid learning	TBD

Critical Issues and Risks


None at this time

School Operational Readiness



Implement updated school operation plans with health and safety procedures installed and transportation and meal distribution solidified.

Leading Indicators

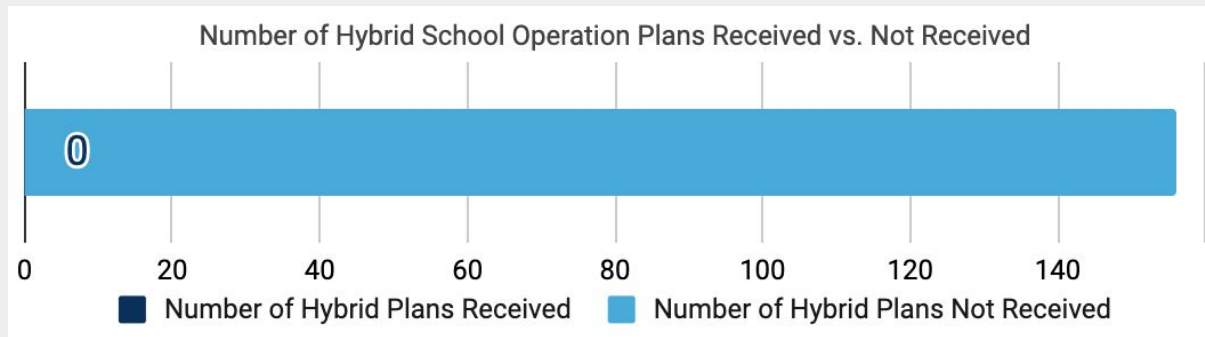

<p>100%</p> <p>% of Health and Safety Supplies Purchased for Q2</p>	<p>TBD</p> <p>Principal Confirmed Receipt of PPE at School</p>
--	---

<p>1,760,000</p> <p>Total PPE Needed for Q2</p>	<p>100,000</p> <p>Total Disinfectant Items Needed for Q2</p>
--	---

<p>107,375</p> <p>Total Number of Students Served Meals in SY20-21</p>	<p>1,082,926</p> <p>Total Number of Meals Distributed in SY20-21</p>
---	---

Upcoming Key Activities

Activities	Deadline
Complete hybrid school operation plans	TBD

Critical Issues and Risks

None at this time

Monitoring Student Outcomes

Student attendance rate (grades K-8 ADA) 90%

Student attendance rate (grades 9-12 ADA) 92%

% of all students attending 95%+ of enrolled days through October 64%

% of students testing at-target on AimsWeb and STAR during fall assessment window (closed Oct. 23) ELA: 33%
Math: 39%

of parent/guardians responding to fall digital learning survey (open from Sept 24-Oct 15) 8,972 parent/guardians from 307 District & Charter Schools

% of parent/guardians who responded to the survey who are satisfied with digital learning so far 35% yes, 30% somewhat, 34% no, 1% don't know
